

Personal




Personal Paraguay Phase 2 Weekly Updates



 **quantiphi**
Solving What Matters
TELECOM



Agenda

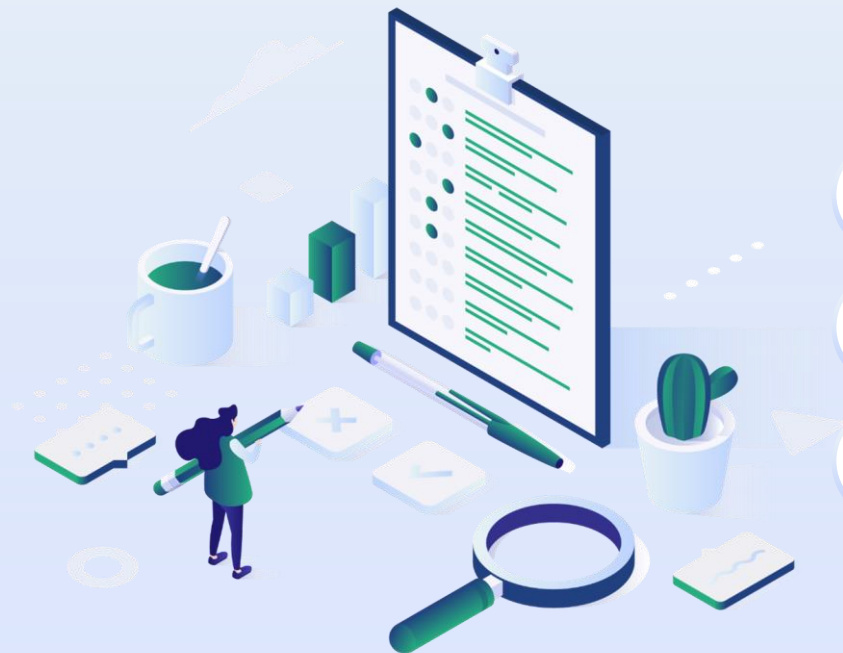

Weekly updates




Project timeline



Appendix

01

Weekly Updates

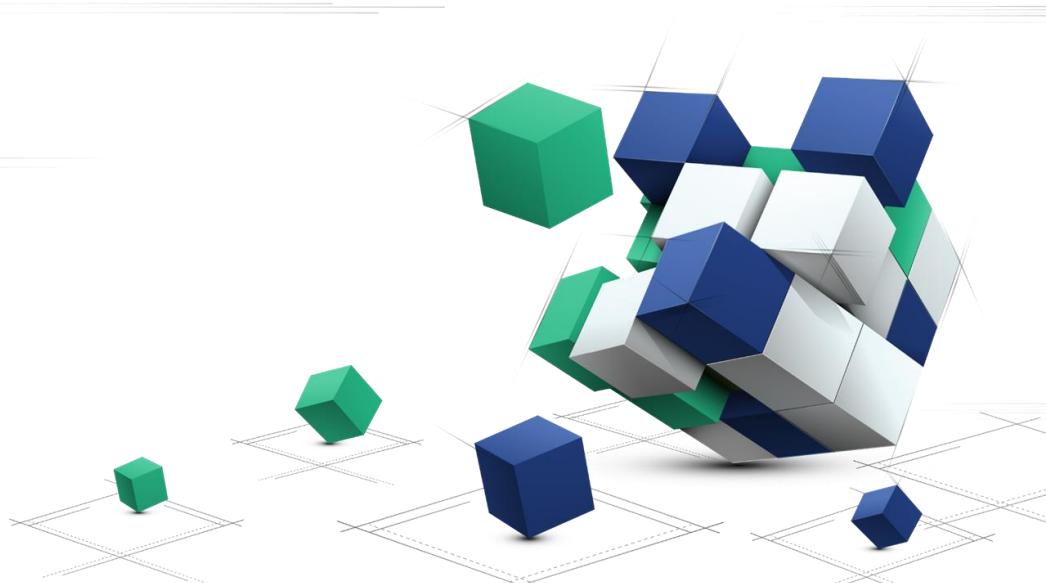

Weekly Project Report Week 15 [June 08 - June 14]



Task Progress

- **Data Validation completed for prod**
- **Stabilisation phase successfully completed.**
- **Closure call with the Personal stakeholders completed where Quantiphi team provided an update on the engagement highlights and the future roadmap for the Personal Team.**



Next Steps

- Change Order approval by the Personal Team
- Feedback and Testimonial to be shared by the Personal Team



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 13 | 14 | 15 | 16

Planned  

Actual  

Achieved Milestones

- Data Validation completed for prod
- Stabilisation phase successfully completed.
- Closure call with the Personal stakeholders completed where Quantiphi team provided an update on the engagement highlights and the future roadmap for the Personal Team.

Planned Milestones

- Change Order approval by the Personal Team
- Feedback and Testimonial to be shared by the Personal Team



Open Items and Risks

Open Risks
• NA

Open Items:
• NA

Completed Tasks

Tasks	Status/Dependencies
GCP governance model	Completed
Setup Cloud identity & Access management	Completed
Setup project, billing & organisation policies	Completed
Cloud security command	Completed
Establish network foundations (VPC, Cloud VPN, Network Security)	Completed
Understood data ingestion process from Postgres & overview of on-prem system and flow of data transformations used in SSIS Packages	Completed
GCP KT Sessions Link	Completed
Data Profiling and Data governance	Completed
Setup native GCP security controls	Completed
Enable required GCP services	Completed
Configure data backup & archival policies	Completed

Completed Tasks


Tasks	Status/Dependencies
Design & setup CI/CD pipelines	Completed
Integration with source systems	Completed
Data model creation(Data Ingestion process from postgres, Flow of data transformations in SSIS packages)	Completed
Data schema design (working on redesigning of SQLs for data use case)	Completed
Design & setup CI/CD pipelines	Completed
Setup Logging & Monitoring	Completed
Design & Creation of Terraform scripts to automate infrastructure deployment (IaC)	Completed
Configure Dev, Pre-Prod & Prod environments (Infrastructure foundations)	Completed
Ingestion pipeline setup	Completed
Transformation pipeline build based on policies shared	Completed
Consumption pipeline setup	Completed

Completed Tasks


Tasks	Status/Dependencies
AD/LDAP Integration with Cloud Identity	Completed
Data validation framework	Completed
Validation by Quantiphi team	Completed
Production Go Live, Cutover & Sign Off	Completed
Hypercare Support & Handover	Completed

02


Project Timeline

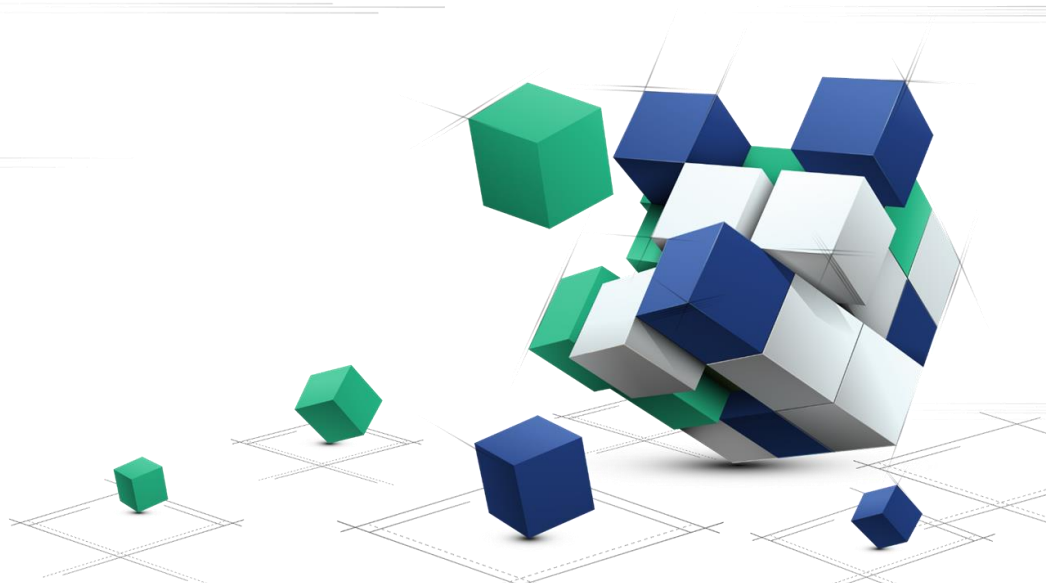


Planned timeline

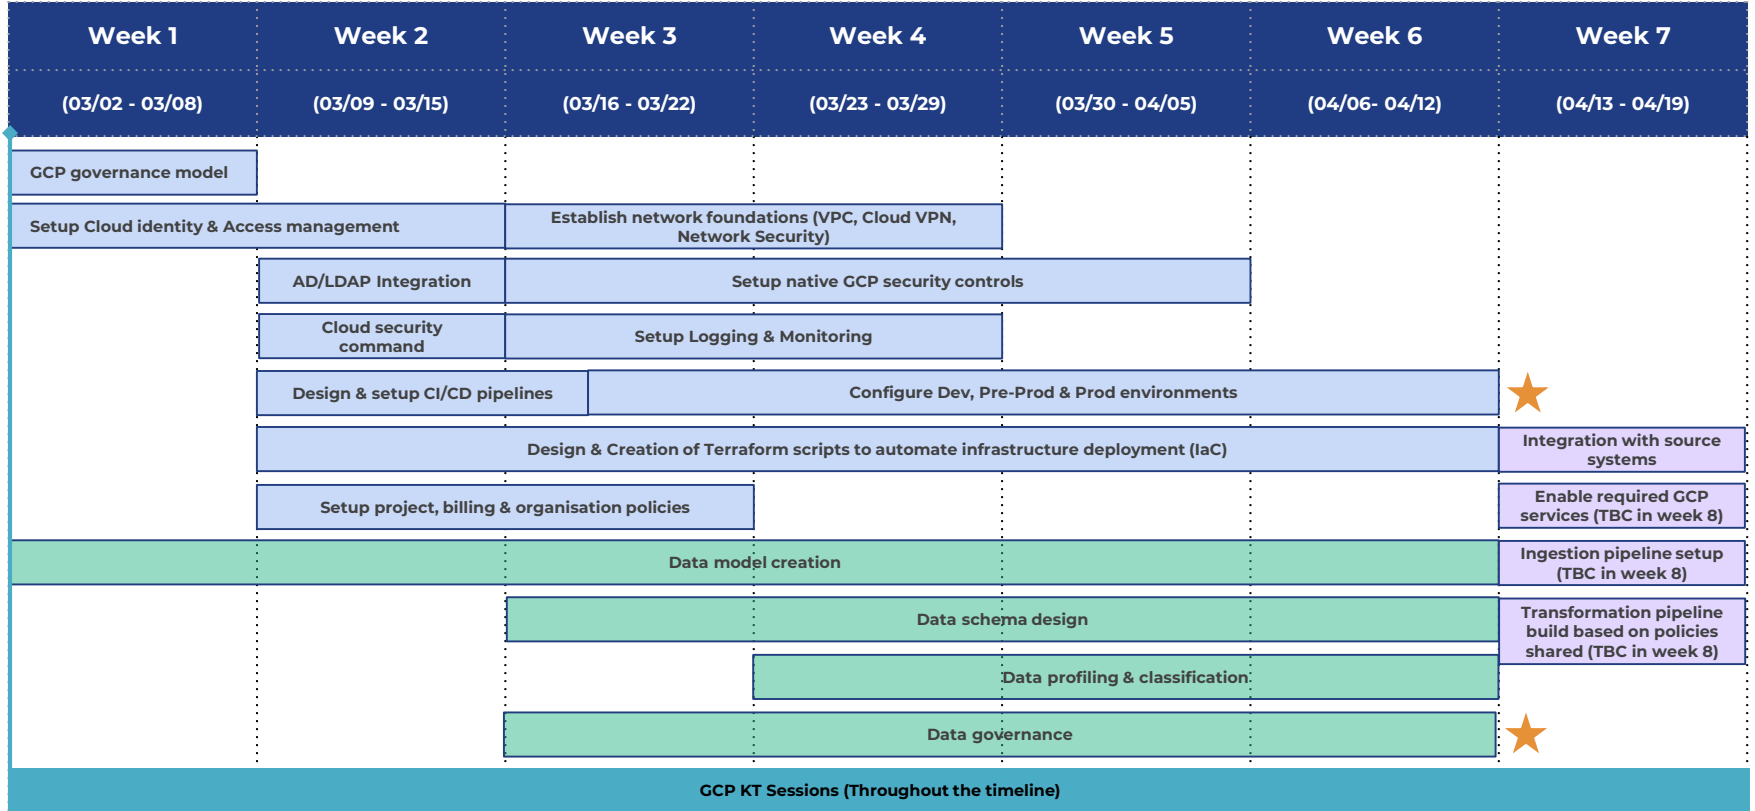


START
(03/02/2022)





Planned timeline

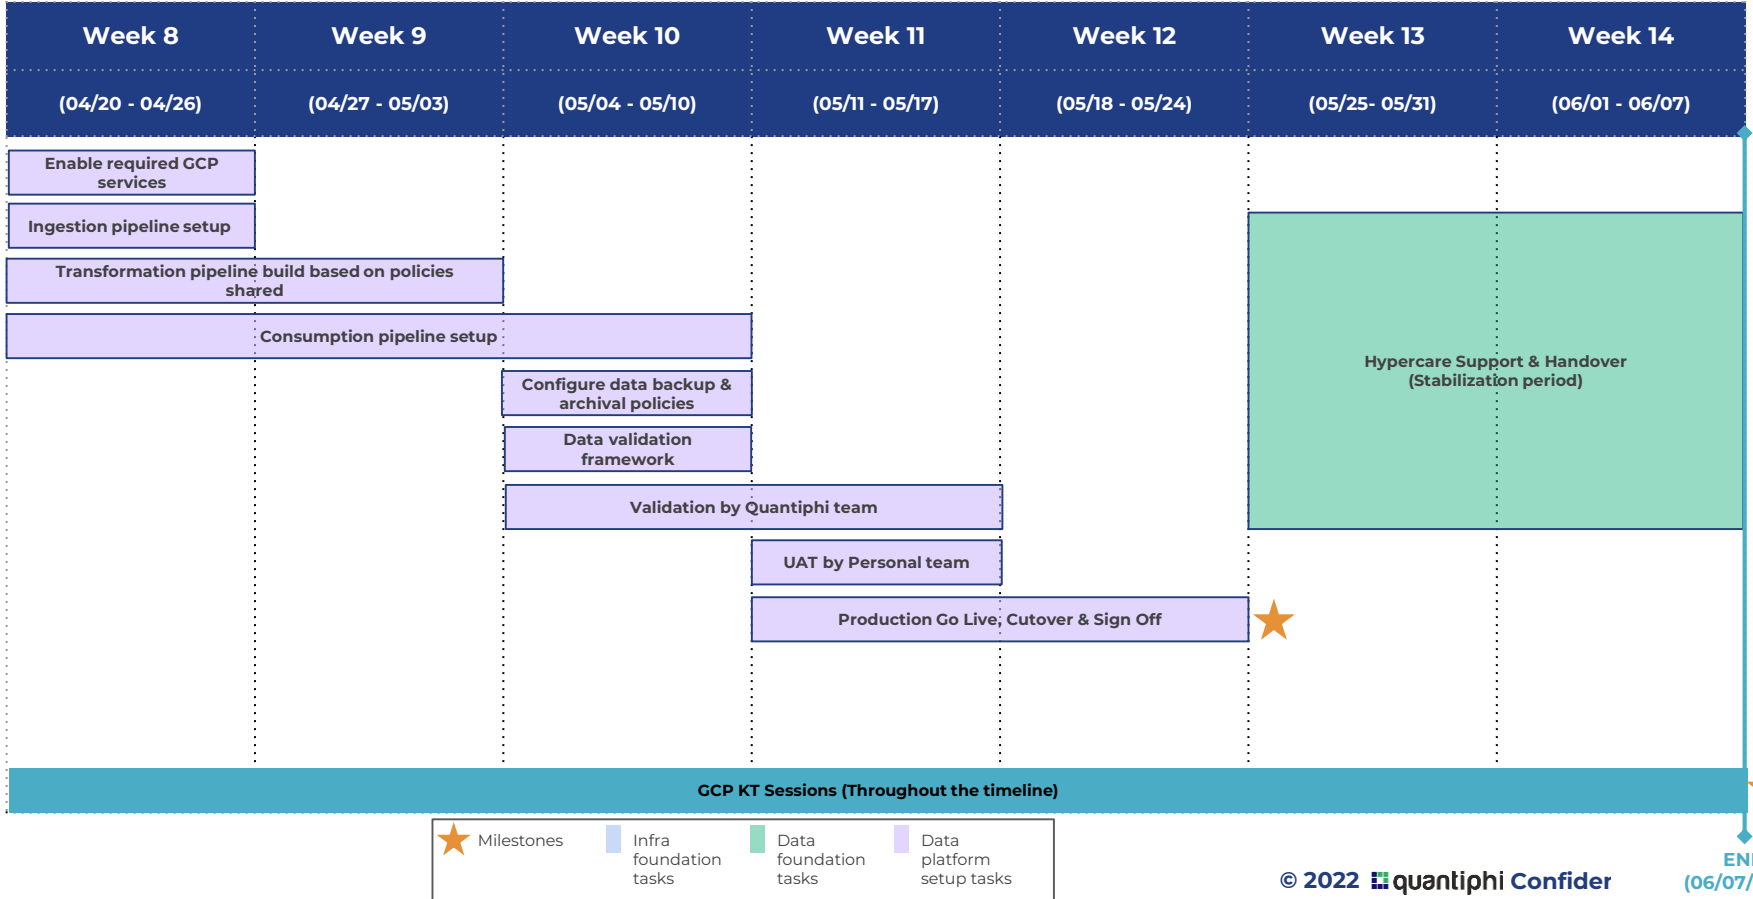

Timeline

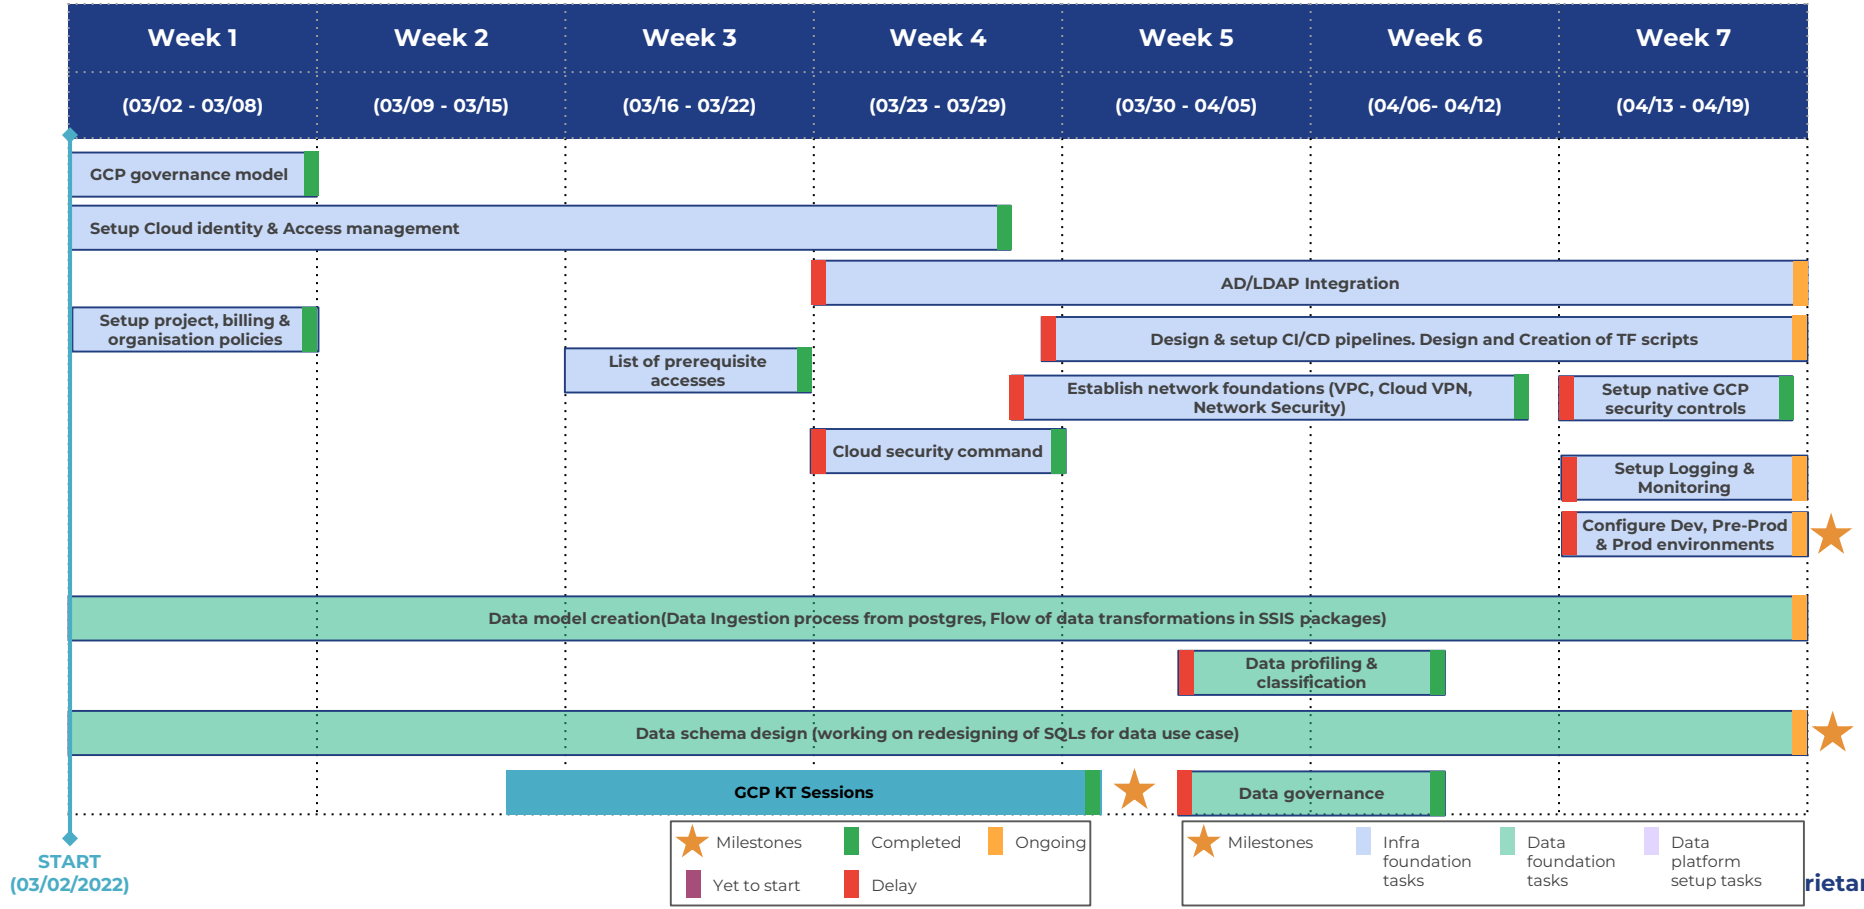

Timeline (Validation parallelly with Stabilization)

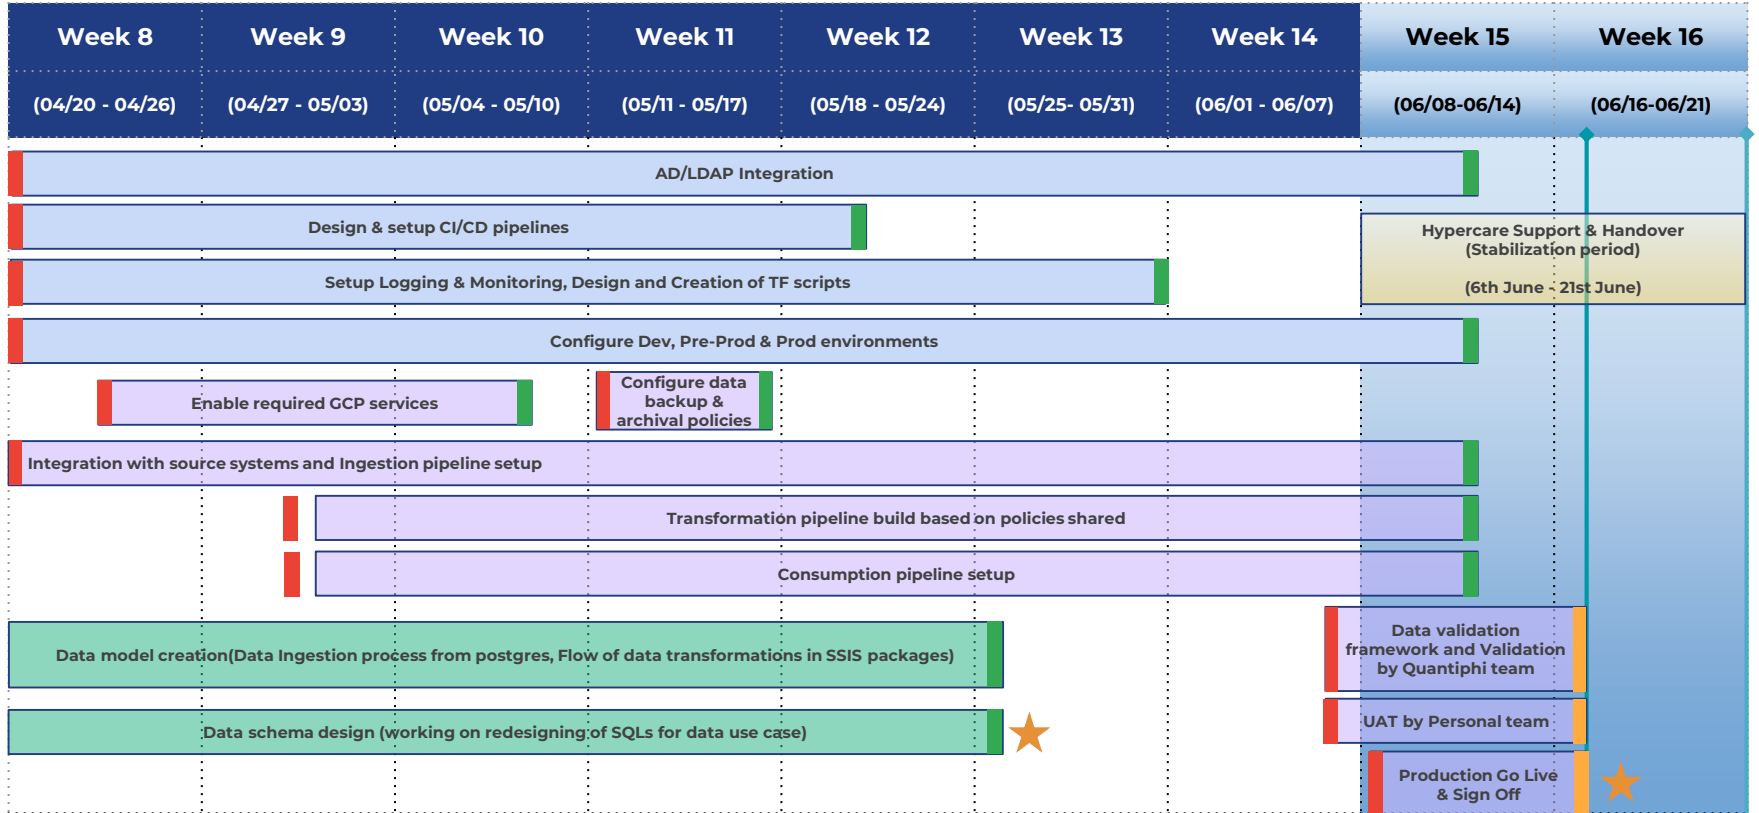

****This timeline is updated considering all the blockers are resolved latest by 20th May and there are no additional blockers**

Muchas Gracias Thank You

Explore More at

www.quantiphi.com

Follow us on:



03

Appendix



Implementation Plan

Tasks	Sub tasks	Status	Progress/Dependencies
Design GCP governance model	Designing Resource Hierarchy	Completed	
	Set up Organization Policies & Folder and Project Level Policies		
Setup Cloud identity & Access management	Creation of Groups & Users	Completed	
	Set up access management to the Groups and Users		
AD/LDAP Integration with Cloud Identity	Integration of Onprem AD with GCP cloud Identity service	Completed	
Implement Cloud Security Command Center	Implementing csc on the services	Completed	
Design & setup CI/CD pipelines	Implementing cloud native service i.e., cloud build for CI & CD	Completed	
	Creation build pipelines to fetch the code from repo	Completed	
	creation release pipelines to deliver the code to dev ,pre prod, prod env	Completed	
Design & Creation of Terraform scripts to automate infrastructure deployment (IaC)	Creation terraform scripts for all services	Completed	
Setup project, billing & organisation policies	Set up project billings	Completed	
Establish network foundations (VPC, Cloud VPN, Network Security)	Setting up cloud vpn for making communication between onprem to gcp	Completed	
Setup native GCP security controls	Setting up firewall rules	Completed	
	Setting vpc service controls	Completed	

Implementation Plan

Tasks	Sub tasks	Status	Progress/Dependencies
Setup Logging & Monitoring	Setting up centralized project for logging and monitoring	Completed	
	Creation of monitoring dashboards,alert policies and uptime checks	Completed	
Configure Dev, Pre-Prod & Prod environments	All the tasks will be implemented in Dev-->PreProd-->Prod	Completed	
DATA FOUNDATION			
Data model creation	Data types compatible with the data Initialization of schemas for both the data sources, postgresql and the CSV files	Completed	Updated schema shared. Need final approval. ETA : To be closed after the SQL script is shared and schema is updated accordingly Completed on 05/27
Data schema design	Deciding the logical schema of all the tables and flow diagrams of the data ingestion	Completed	
Data profiling & classification	According to the necessity, data cleaning will be done.	Completed	
Data governance	Data governance strategy will be explained to Personal team using Data Catalog. If Needed, it will be implemented	Completed	

Implementation Plan

Tasks	Sub tasks	Status	Progress/Dependencies
DATA PLATFORM SETUP			
Integration with source systems	Test connection with postgres and Network shared drive from composer env	Completed	
Enable required GCP services	Enable services in Dev manually	Completed	
	Create terraform scripts to enable GCP services in prd	Completed	
Ingestion pipeline setup	Create buckets and datasets	Completed	
	Create tables in BQ	Completed	
	Create composer DAGS - Composer DAG creation for ingesting data from postgres tables and testing for all raw tables - Composer DAG creation for ingesting data from network shared drive and testing for all raw tables - Composer DAG creation for copying data to BQ tables - Composer DAG to transform data	Completed	
	Integration with Secret manager	Completed	

Implementation Plan

Tasks	Sub tasks	Status	Progress/Dependencies
Transformation pipeline build based on policies shared		Completed	
Consumption pipeline setup	Pipeline orchestration - scheduling	Completed	
Configure data backup & archival policies	Configure a lifecycle policy for data archival(dev+prod)	Completed	
Data validation framework	Deciding the template or any specific conditions/parameters based on which data in the warehouse will be validated Brief Validation reports	Completed	
Validation by Quantiphi team		Completed	
UAT by Personal team			
Production Go Live, Cutover & Sign Off	To promote everything From dev, test to prod	Completed	
Hypercare Support & Handover	- Assist Personal stakeholders as they start adopting and operating the new platform - Address any technical questions - Bug fixes - Resolve any configuration issue that may arise during this period	Completed	

****The ETA dates for each task is updated considering all the blockers are resolved latest by 20th May and there are no additional blockers.**

Weekly Project Report Week 15 [June 08 - June 14]



Task Progress

- **Transformation pipeline build based on policies shared**
- **Consumption pipeline setup**
- **Ingestion pipeline testing completed all env.**
- **Data validation for dev and pre prod completed.**
- **Prod migration completed successfully**
- Prod data validation on going.
- Quantiphi team working on the TDD review provided by Personal team.
- Started with stabilization period sessions (GCP administration)



Next Steps

- Overview call on Azure AD sync
- Data Validation to be completed for prod
- Completion of stabilization period meetings and final sign off



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 13 | 14 | 15 | 16

Planned   

Actual   

Achieved Milestones

- Transformation pipeline build based on policies shared
- Consumption pipeline setup
- Ingestion pipeline testing completed all env.
- Data validation for dev and pre prod completed.
- Prod migration completed successfully

Planned Milestones

- Overview call on Azure AD sync
- Data Validation to be completed for prod
- Completion of stabilization period meetings and final sign off



Open Items and Risks

Open Risks
• NA

Open Items:
• NA

Weekly Project Report Week 14 [June 01 - June 07]



Task Progress

- **TDD document completed for both Infra and Data and sent for Personal team's review.**
- **Design and Creation of TF script**
- **Setup Logging & Monitoring**
- **Connection to ATLASHIS db and ODS for data validation established. .**
- **Ingestion pipeline testing ongoing for dev**



Next Steps

- Overview call on Azure AD sync
- Ingestion pipeline testing
- Transformation pipeline build based on policies shared and Consumption pipeline setup
- Data Validation to be completed..



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 13 | 14 | 15 | 16

Planned   

Actual   

Achieved Milestones

- TDD document completed for both Infra and Data and sent for Personal team's review.
- Design and Creation of TF script
- Setup Logging & Monitoring
- Connection to ATLASHIS db and ODS for data validation established. .
- Ingestion pipeline testing completed for dev.

Planned Milestones

- Overview call on Azure AD sync
- Ingestion pipeline testing
- Transformation pipeline build based on policies shared and Consumption pipeline setup
- Data Validation to be completed..



Open Items and Risks

Open Risks
• NA

Open Items:
• NA

Weekly Project Report Week 13 [May 25 - May 31]



Task Progress

- **TDD document completed for infra foundations and sent for Personal team's review.**
- **Data schema design and Data model creation - Data foundation completed**
- **Setup Logging & Monitoring - Final policies updated after schema finalisation**
- **DNS connection between on prem and GCP established**
- **Integration with source systems completed.**
- Ingestion Pipeline setup is in progress.



Next Steps

- Overview call on Azure AD sync
- BQ and Composer TF scripts to be implemented in pre prod and prod
- Ingestion pipeline testing
- Transformation pipeline build based on policies shared and Consumption pipeline setup
- Data Validation to be completed..
- Completion of TDD documentation for Data



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 13 | 14 | 15 | 16



Achieved Milestones

- TDD document completed for infra foundations and sent for Personal team's review.
- Data schema design and Data model creation - Data foundation completed
- Setup Logging & Monitoring - Final policies updated after schema finalisation
- DNS connection between on prem and GCP established
- Integration with source systems completed.

Planned Milestones

- Overview call on Azure AD sync
- BQ and Composer TF scripts to be implemented in pre prod and prod
- Ingestion pipeline testing
- Transformation pipeline build based on policies shared and Consumption pipeline setup
- Data Validation to be completed..
- Completion of TDD documentation for Data



Open Items and Risks

Open Risks

- Based on the dependencies that are yet to be resolved, we have re-estimated a delay of two weeks. This is considering that there are no additional blockers

Open Items:

- Personal is working internally to complete the following open action items: Access to ODS and SMTP details. Personal team working on the Ingestion pipeline setup with the Google team.. Quantiphi team reviewing the VPC logs.

Weekly Project Report Week 12 [May 18 - May 24]



Task Progress

- **CI/CD implementation and testing completed in all environments.**
- **Ingestion pipeline testing initiated.**
- **Integration with source systems.**
- Technical Design Document Update is in progress.
- Final schema shared and approved. Schema to be updated according to the SQL script of final pack summary table.



Next Steps

- Overview call on Azure AD sync
- Final schema approval
- Completion of infrastructure foundations
- Data foundation tasks to be completed.
- Ingestion pipeline testing
- Transformation pipeline build and consumption pipeline setup
- Data Validation framework
- Completion of TDD documentation



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 9 | 10 | 11 | 12

Planned   

Actual   

Achieved Milestones

- CI/CD implementation and testing completed in all environments.
- Ingestion pipeline testing initiated.
- Integration with source systems.

Planned Milestones

- Overview call on Azure AD sync
- Final schema approval
- Completion of infrastructure foundations
- Data foundation tasks to be completed.
- Ingestion pipeline testing
- Transformation pipeline build and consumption pipeline setup
- Data Validation framework
- Completion of TDD documentation



Open Items and Risks

Open Risks

- Based on the dependencies that are yet to be resolved, we have re-estimated a delay of two weeks. This is considering that there are no additional blockers

Open Items:

- Personal is working internally to complete the following open action items: Access to ODS and ATLASHIS DB

Weekly Project Report Week 11 [May 11 - May 17]



Task Progress

- **CI/CD implementation completed in all environments.** Pre prod and prod slaves not working as they are not able to reach gitlab
- **Updated folder structure and underlying projects as per the updated Resource Hierarchy**
- **Composer IP whitelisting completed.**
- **Azure AD sync completed and validated in PoC**
- Ingestion script is ready to test. Awaiting on the Postgres credentials
- Technical Design Document Update is in progress.
- Final schema shared. Awaiting on the feedback



Next Steps

- Overview call on Azure AD sync
- Final schema approval
- Completion of infrastructure foundations
- Data foundation tasks to be completed.
- Ingestion pipeline testing
- Integration with source systems
- Completion of TDD documentation



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 9 | 10 | 11 | 12



Achieved Milestones

- CI/CD implementation completed in all environments.
- Updated folder structure and underlying projects as per the updated Resource Hierarchy
- Composer IP whitelisting completed.
- Azure AD sync completed and validated in PoC
- Ingestion script is ready to test.

Planned Milestones

- Overview call on Azure AD sync
- Final schema approval
- Completion of infrastructure foundations
- Data foundation tasks to be completed.
- Ingestion pipeline testing
- Integration with source systems
- Completion of TDD documentation



Open Items and Risks

Open Risks

- Based on the dependencies that are yet to be resolved, we have re-estimated a delay of two weeks. This is considering that there are no additional blockers

Open Items:

- Personal is working internally to complete the following open action items: Whitelisting of subnets and will be sharing SFTP server IP and host name, Postgres credentials for composer access, access to ODS and ATLASHIS DB and validation script for Postgres and SQL server data

Weekly Project Report Week 10 [May 04 - May 10]



Task Progress

- **CI/CD implementation completed in all environments.** Personal team working on the firewall rules for Gitlab Jenkins connection
- **TF script implemented for Cloud Storage buckets in pre prod and prod environments**
- **Updated folder structure and underlying projects as per the updated Resource Hierarchy.**
- Ingestion script is ready to test. Awaiting on the Postgres credentials
- Technical Design Document Update is in progress.
- Azure AD integration to GCP is ongoing



Next Steps

- Azure AD integration to GCP to be completed
- Final schema approval
- Completion of infrastructure foundations
- Data foundation tasks to be completed.
- Ingestion pipeline testing
- Integration with source systems
- Completion of TDD documentation



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 9 | 10 | 11 | 12

Planned   

Actual   

Achieved Milestones

- CI/CD implementation completed in all environments.
- TF script implemented for Cloud Storage buckets in pre prod and prod environments
- Updated folder structure and underlying projects as per the updated Resource Hierarchy.

Planned Milestones

- Azure AD integration to GCP to be completed
- Final schema approval
- Completion of infrastructure foundations
- Data foundation tasks to be completed.
- Ingestion pipeline testing
- Integration with source systems
- Completion of TDD documentation



Open Items and Risks

Open Risks

- Based on the dependencies that are yet to be resolved, we have estimated a delay of one week. This is considering that there are no additional blockers

Open Items:

- Personal is working internally to complete the following open action items: Whitelisting of subnets and will be sharing SFTP server IP and host name, Postgres credentials for composer access, access to ODS and ATLASHIS DB, additional details of the newly added column, schedule times and email ids

Weekly Project Report Week 09 [Apr 27 - May 03]



Task Progress

- **CI/CD implementation completed in all environments.** Personal team is checking with the security team on a issue regarding Gitlab Jenkins connection
- **TF script for enabling API completed.**
- **Review of the architecture completed and the Resource Hierarchy re-updated.**
- Technical Design Document Update is in progress.
- Azure AD integration to GCP is ongoing



Next Steps

- Azure AD integration to GCP to be completed
- Completion of BQ TF script once schema is finalised
- Data foundation tasks to be completed.
- Initiation of Data platform setup tasks



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 9 | 10 | 11 | 12



Achieved Milestones

- CI/CD implementation completed in all environments.
- TF script for enabling API completed.
- Review of the architecture completed and the Resource Hierarchy re-updated.

Planned Milestones

- Azure AD integration to GCP to be completed
- Completion of BQ TF script once schema is finalised
- Data foundation tasks to be completed.
- Initiation of Data platform setup tasks



Open Items and Risks

Open Risks

- Delay in resolving the dependencies might compromise the stabilization period which is of 2 weeks as per the current plan

Open Items:

- Personal is working internally to complete the following open action items: Mayur's outlook issue, overlapping subnets, Azure AD sync completion and will be sharing SFTP server IP and host name, Postgres credentials for composer access, and Schema and sample CSV files of new parametric tables

Weekly Project Report Week 08 [Apr 20 - April 26]



Task Progress

- **CI/CD implementation completed in all environments.** Awaiting response from the Personal Team on the Webhook timeout increase.
- **TF script for enabling API completed.**
- Technical Design Document Update is in progress.
- Azure AD integration to GCP is ongoing
- Review of the SQLs by the Personal DWH team- Ongoing



Next Steps

- Azure AD integration to GCP to be completed
- Completion of BQ TF script once schema is finalised
- Data foundation tasks to be completed.
- Initiation of Data platform setup tasks



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health



Milestones Completed

Week 5 | 6 | 7 | 8



Achieved Milestones

- CI/CD implementation completed in all environments.
- TF script for enabling API completed.
- Technical Design Document Update is in progress.

Planned Milestones

- Azure AD integration to GCP to be completed.
- CI/CD Pipeline testing.
- Completion of BQ TF script once schema is finalised
- Data foundation tasks to be completed.
- Initiation of Data platform setup tasks
- Review of the SQL by the Personal DWH team to be completed.



Open Items and Risks

Open Risks
NA

Open Items:

- Additional calls required to discuss on mechanism to copy CSV files to SFTP server
- Personal's IT Security team working internally to complete the open action items.

Weekly Project Report Week 07 [Apr 13 - April 19]



Task Progress

- **CI/CD implementation completed in all environments. Testing pending.**
- **Data profiling and data governance - Completed**
- **Setting up VPC service controls- Completed**
- **TF scripts for Cloud Composer and storage bucket are completed**
- **Monitoring dashboards, alert policies and log sinks created**
- Azure AD integration to GCP - Ongoing



Next Steps

- Azure AD integration to GCP to be completed
- Completion of BQ TF script once schema is finalised
- Data foundation tasks to be completed.
- Initiation of Data platform setup tasks



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health 



Milestones Completed

Week 5 | 6 | 7 | 8



Achieved Milestones

- CI/CD implementation completed in all environments.
- Data profiling and data governance completed
- Setting up VPC service controls
- TF scripts for Cloud Composer and storage bucket
- Monitoring dashboards, alert policies and log sinks created

Planned Milestones

- Azure AD integration to GCP to be completed.
- CI/CD Pipeline testing.
- Completion of BQ TF script once schema is finalised
- Data foundation tasks to be completed.
- Initiation of Data platform setup tasks



Open Items and Risks

Open Risks
NA

Open Items:

- Additional calls required to discuss on the first version of schema

Weekly Project Report Week 06 [Apr 06 - April 12]



Task Progress

- **CI/CD implementation in Dev in progress, Jenkins installation - Completed.**
- **Bucket and project names clarified by the Personal Team.**
- **Data profiling and data governance - Completed**
- Azure AD integration to GCP - Ongoing
- Design & Creation of Terraform scripts in progress - Ongoing



Next Steps

- Azure AD integration to GCP to be completed.
- Design and setup CI/CD pipelines
- Setting up VPC service controls
- Completion of Terraform scripts
- Data foundation tasks to be completed.



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health ●



Milestones Completed

Week 5 | 6 | 7 | 8



Achieved Milestones

- Jenkins installation for CI/CD implementation in Dev is completed.
- Bucket and project names clarified by the Personal Team. Design & Creation of Terraform scripts in progress.
- Data profiling and data governance completed

Planned Milestones

- Azure AD integration to GCP to be completed.
- Design and setup CI/CD pipelines
- Setting up VPC service controls
- Completion of Terraform scripts
- Data foundation tasks to be completed.



Open Items and Risks

Open Risks
• NA

Open Items:

- Additional calls required to understand the business rules and SQLs
- VPN issue to be resolved

Weekly Project Report Week 05 [Mar 30 - April 05]



Task Progress

- GCP KT sessions completed for all the services
- Implementation of Cloud Security Command Center completed.
- Azure AD integration to GCP - ongoing
- VPC and Firewall setup
- Jenkins installation with CI/CD pipeline in progress
- VPN setup completed.



Next Steps

- Azure AD integration to GCP to be completed.
- Design and setup CI/CD pipelines
- Setting up VPC service controls
- Design & Creation of Terraform scripts



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health ●



Milestones Completed

Week 5 | 6 | 7 | 8



Achieved Milestones

- GCP KT completed for all the services
- Implementation of CCCC completed
- Azure AD integration to GCP - ongoing
- VPC and Firewall setup
- Jenkins installation to begin with CI/CD pipeline

Planned Milestones

- Azure AD integration to GCP to be completed.
- Design and setup CI/CD pipelines
- VPN setup and Setting up VPC service controls
- Design & Creation of Terraform scripts



Open Items and Risks

Open Risks
• NA

Open Items:
Additional calls required to understand the business rules and SQLs

Weekly Project Report Week 04 [Mar 23 - Mar 29]



Task Progress

- GCP KT sessions completed for the below services:
-Introduction to GCP, BigQuery, Cloud Storage, PubSub, Cloud Composer, Cloud VPC, Cloud VPN, Stackdriver Logging & Monitoring
- Design the below services via Terraform scripts completed
 - Set up project billings
 - Set up Organization Policies & Folder and Project Level Policies
- Setup Cloud identity & Access management



Next Steps

- GCP KT sessions to be continued.
- Azure AD integration to GCP to be completed.
- Implement Cloud Security Command Center
- VPC and CI/CD pipelines setup to be completed.



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health



Milestones Completed

Week 1 | 2 | 3 | 4

Planned

Actual

Achieved Milestones

- GCP KT sessions completed for the below services: **Introduction to GCP, BigQuery, Cloud Storage, PubSub, Cloud Composer, Cloud VPC & VPN, Logging & Monitoring**
- Design the below services via Terraform scripts completed
 - Set up project billings, Org Policies and Folder and Setup Cloud identity & Access management

Planned Milestones

- GCP KT sessions continuation
- AD/LDAP Integration with Cloud Identity to be completed.
- Implementation of CSCC
- VPC and CI/CD pipelines setup to be completed.



Open Items and Risks

Open Risks
• NA

Open Items:

Additional calls required to understand the on prem data transformation

Weekly Project Report Week 03 [Mar 16 - Mar 22]



Task Progress

- GCP KT sessions completed for the below services:
 - Introduction to GCP
 - BigQuery
 - Cloud Storage
 - PubSub
 - Cloud Composer
- Design the below services via Terraform scripts completed
 - Set up project billings
 - Set up Organization Policies & Folder and Project Level Policies
- Setup Cloud identity & Access management



Next Steps

- GCP KT sessions to be continued.
- Azure AD integration to GCP to be completed.
- VPC and CI/CD pipelines setup to be completed.



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health



Milestones Completed

Week 1 | 2 | 3 | 4

Planned

Actual

Achieved Milestones

- GCP KT sessions completed for the below services:
 - Introduction to GCP, BigQuery, Cloud Storage, PubSub, Cloud Composer
- Design the below services via Terraform scripts completed
 - Set up project billings, Org Policies and Folder and Setup Cloud identity & Access management

Planned Milestones

- GCP KT sessions to be continued.
- Azure AD integration to GCP to be completed.
- VPC and CI/CD pipelines setup to be completed.



Open Items and Risks

Open Risks
NA

Open Items:
NA

Weekly Project Report Week 02 [Mar 09 - Mar 15]



Task Progress

- Access granted to the Data team
- Team completed the task of designing resource hierarchy in the GCP console as well as in Terraform
- Project billings and Org Policies setup completed in the GCP console.
- GCP KT session plan confirmation by the Personal Team



Next Steps

- GCP KT sessions to be started
- Design the below services via Terraform scripts
 - Set up project billings
 - Set up Organization Policies & Folder and Project Level Policies
- Setup Cloud identity & Access management




Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health



Milestones Completed



Achieved Milestones

1. Accesses to the Personal's environment for Data team
2. Resource Hierarchy, Project billings and Org Policies setup in GCP Console completed.
3. GCP KT sessions plan confirmation by the Personal Team

Planned Milestones

- GCP KT sessions kick off
- Design the below services via Terraform scripts
 - Set up project billings
 - Set up Organization Policies & Folder and Project Level Policies
- Setup Cloud identity & Access management



Open Items and Risks

Open Risks
• NA

Open Items:
NA

Weekly Project Report Week 01 [Mar 02 - Mar 08]



Task Progress

- SOW signed with the Personal team.
- Kick off with the Personal Stakeholders Completed. (Mar 03 to be considered as Day 1)
- GCP Audit & Logging Setup
- Non org operation project setup
- Access granted to the Infra team.
- Team started on the task of designing resource hierarchy



Next Steps

- Planning of GCP KT sessions
- Design Resource Hierarchy
- Set up project billings
- Set up Organization Policies & Folder and Project Level Policies



Summary & Overall Health

- Quantiphi Team is having Daily Huddles and has planned technical knowledge transfer sessions with the Personal Team to discuss the progress updates daily
- Project Overall Health



Milestones Completed

Week 1 | 2 | 3 | 4

Planned   

Actual   

Achieved Milestones

1. Accesses to the Personal's environment for Infra team
2. GCP Audit & Logging Setup
3. Non org operation project setup

Planned Milestones

- Planning of GCP KT sessions
- Design Resource Hierarchy
- Set up project billings
- Set up Organization Policies & Folder and Project Level Policies



Open Items and Risks

Open Risks
• NA

Open Items:
NA
